



## **Doral Central Park Amphitheater**

December 8th, 2023



# Table of Contents

Program Overview	
Project Completed	4
Program Progress Report	5
Timeline	6
<b>Project Information &amp; Status</b>	
Doral Central Park	7
Work Completed	8-11
Upcoming Work	12
Doral Cultural Arts Center	13
Current Status	14
Trails Network	15
• Cumont Status	16



**AECOM** 

## **Program Overview**

On June 13, 2018, the City unanimously adopted Resolution No. 18-112 by the City Council authorizing the City to hold a bond referendum election for the purpose of determining whether most qualified electors voting in the election would approve the issuance of the City's general obligation bonds to finance the cost of the Parks and Recreation Projects.


On November 6, 2018, the City of Doral residents voted to approve the referendum authorizing the City to issue general obligation bonds in an amount not to exceed \$150,000,000. These bonds are to be utilized for upgrading and building a system of world class parks, natural areas and recreational facilities.

The Bond Referendum authorized the financing of the construction and improvement of parks and recreational facilities with safety features, including, but not limited to, green spaces, community centers, cultural amenities, aquatic facility, playgrounds, sports fields and approximately five miles of walking/cycling trails.

The General Obligation Bond includes the following projects: the redevelopment of Doral Central Park, Doral Meadow Park renovation, the construction of the Doral Cultural Arts Center, the construction of Doral White Course Park, Morgan Levy Park improvements, lighting improvements for Trails and Tails Park, and bikeways/lighting improvements for various Trails Networks.



## **Projects Completed**



#### **Morgan Levy Park** Completed – May 2021

Morgan Levy Park is located at 5300 NW 102nd Avenue, Doral, FL. This project involved the removal and replacement of existing flooring, new millwork, painting, addition of a grease interceptor, and ADA accessible routes to picnic areas. In addition, the project also included the transition to high-efficiency LED fixtures in



#### **Doral Meadow Park**

Completed - Aug 2021

The park is located at 11555 NW 58th Street, Doral, FL. The project included the enclosure of an existing outdoor patio space to provide 800 square feet of indoor recreation area with a new HVAC system. In addition, the existing building renovation included a high-tech conference room, a kitchenette, façade treatments, an indoor trophy case, modernized bathrooms, and a multi-purpose outdoor plaza.



#### **Doral White Course Park**

Completed – July 2022

This Park is located at 8425 NW 41st Street in Doral, FL. This new park includes a shaded playground, waterfront plaza, outdoor fitness stations, a multi-purpose green space area, fenced-off dog area, restrooms, and shelters. The park has landscape lighting with general overhead and walkway lighting and security cameras. A new boardwalk will connect this park to the Downtown Doral area.



#### Trails & Tails Park

Completed – July 2022

The park is located at 11645 NW 50th Street, Doral FL. This project included the installation of light fixtures in dog areas, parking lot, and playground to increase security and provide for expanded park hours. In addition, additional security cameras will be added to the facility.



#### **Doral Cultural Arts Center**

Completed – Summer 2023 (Pending corrective work)


The Doral Cultural Arts Center site is located at 8363 NW 53 St. Doral FL 33166. adjacent to the City of Doral Government Center. This facility serves to celebrate the variety of cultures, arts, and experiences that make Doral so unique. Features include a large art gallery space, multi-purpose room, rooftop plaza, outdoor courtyard, catering room, and public restrooms.



### **Program Progress Report**

DORAL PARKS BOND BUDGET SUMMARY								
Dec-23		Α		В		С	D	E
Projects	C	Original Program Budgets (NOV 2019)		Budgeted Sub-Total		Expended to Date	Encumbered	Available (B-C-D)
Doral Central Park	\$	119,000,000.00	\$	167,956,872.53	\$	88,094,560.54	\$ 61,628,201.76	\$ 18,234,110.23
Doral Cultural Arts Center	\$	9,800,000.00	\$	10,890,911.97	\$	10,851,787.40	\$ 59,751.65	\$ (20,627.08)
Doral White Course Park	\$	4,100,000.00	\$	4,024,273.12	\$	3,971,748.65	\$ 16,371.85	\$ 36,152.62
Morgan Levy Park	\$	143,000.00	\$	701,439.03	\$	701,439.03	\$	\$ -
Trails and Tails Park	\$	926,000.00	\$	996,140.65	\$	910,649.79	\$ 56,033.48	\$ 29,457.38
Doral Pedestrian Bridge (Canceled)	\$	3,500,000.00	\$	160,633.80	\$	160,633.80	\$ -	\$ -
Trails Network	\$	3,900,000.00	\$	2,336,495.92	\$	336,495.92	\$ 247,677.10	\$ 1,752,322.90
Doral Meadow Park	\$	1,500,000.00	\$	1,737,184.70	\$	1,607,384.70	\$ 0.00	\$ 129,800.00
Administrative Cost	\$	6,900,000.00	\$	8,078,040.95	\$	6,364,867.99	\$ 531,386.46	\$ 1,181,786.50
Potential Savings	\$	-	\$	2,806,976.33	\$	-	\$ -	\$ 2,806,976.33
	C	Original Program Budgets (NOV 2019)		Budgeted Sub-Total		Expended to Date	Encumbered	Available (B-C-D)
TOTALS:	\$	149,769,000.00	\$	199,688,969.00	\$	112,999,567.82	\$ 62,539,422.30	\$ 24,149,978.88

#### **Budget Sub-Total**

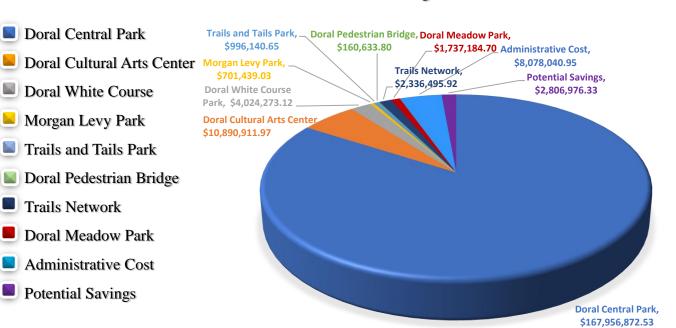





Project	Start Date	Finish Date
Doral Central Park	Feb 2020	Jan/Feb 2025
Doral Cultural Arts Center	Jul 2019	Summer 2023
Doral Meadow Park	Nov 2019	Aug 2021
Doral White Course Park	Sep 2019	Jul 2022
Morgan Levy Park	Nov 2019	May 2021
Trails & Tails Park	Dec 2019	Jul 2022
Trails Network – Phase 1 (Trails)	Apr 2020	Mar 2022
Trails Network – Phase 2 (Lighting)	Jul 2023	TBD



## **Doral Central Park**

#### **Project Information & Status**

Location: 3005 NW 92<sup>nd</sup> Ave.


Doral FL 33172

**Budget:** \$167,956,872.53

**Status:** Under Construction


#### **Program Overview**

Doral Central Park is located at 3005 NW 92nd Avenue. The site is situated on 78 acres of which approximately 21 are the lake. It will be the largest park in the City, and one of the largest in the region. The park includes an 80,000 SF Community Center, Aquatics Center, meandering paved paths connecting tennis and basketball courts, picnic pavilions, playgrounds, beach volleyball courts, multi-purpose fields, skatepark and pump track, as well as an open-air Amphitheater for community and large-scale events. The lake will also have a canoe/kayak/paddleboard launch and boardwalk. Landscaping will add to the enjoyment of the park adding more shaded areas and pleasant views.

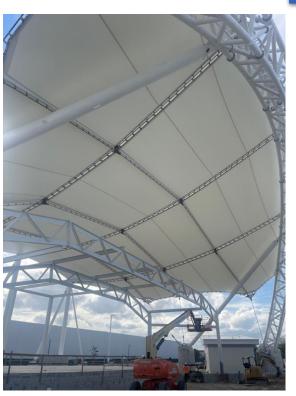

Amphitheater


Project Phase	Start Date	Finish Date
Procurement Process	Feb 2020	May 2020
Design	Apr 2020	Mar 2022
Phase 2 & 3 Construction	Aug 2022	Summer 2024
Phase 4 Construction	Mar 2023	Winter 2024
Closeout Project	Dec 2024	Jan/Feb 2025

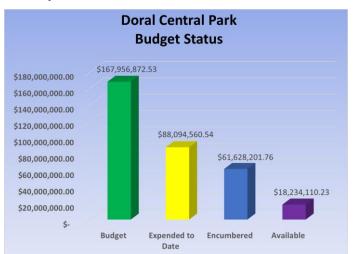



## **Doral Central Park**

Work completed in December 2023

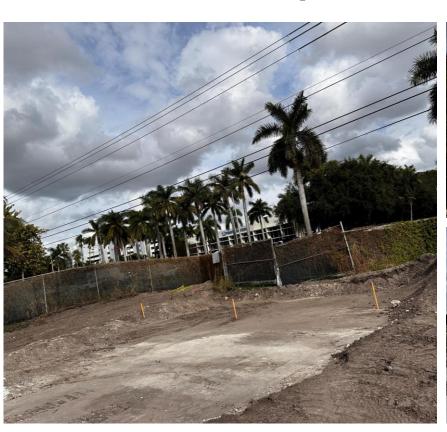





#### Phase 1–71% Complete

- Civil work continues at phase 4 parking lot
- Asphalt poured at west side of Aquatics
- Grading continues at multipurpose field



## Doral Central Park

#### Work completed in December 2023









Phase 2/3 - 59% Complete

#### Amphitheater – 86%

- Seat wall waterproofing work began
- Final grading work at lawn area to begin, as well as preparing lower seating area for concrete slab
- Stucco work began and continues around amphitheater

#### Restroom Buildings – 74%

- Final electrical and mechanical work complete, with drywall work to be completed in January

#### Landscaping/Sidewalks – 31%

-Work continues with trees being installed along sidewalks, and sidewalks being poured



## Doral Central Park

Work completed in December 2023



#### Phase 4 – Community Center - 55% Complete

#### **Interior Space**

- Overhead mechanical ductwork being installed at level 1. Level 2 duct material staged to begin install.
- Framing at level 1 complete. At level 2 90% complete.
- Fireproofing at basketball courts 50% complete
- Office spaces MEP in wall rough complete, insulation installed, with drywall work and drop ceiling install to begin January/February

#### Exterior façade

- Retaining seat wall east side of the community center, rebar and formwork began install.
- Exterior stucco work continues along the north and east façades.
- Painting of exterior walls began at west and south façades.

aecom



## Doral Central Park

Work completed in December 2023









Phase 4 – Aquatics Center – 38% Complete

#### Competition pool/Support Building/Grandstands

- Myrtha system material arrived to begin install in January
- Grand Stands Structural shell erected
- Support building steel roof structure assembly began

#### Leisure Pool/Wading Pool

- Concrete walls and base poured at leisure pool
- Concrete base poured at wading pool, pending walls to be poured in January

aecom



## Doral Central Park

#### **Upcoming Work**



#### Phase 1

- MOT and 87th Ave drainage work to begin in January.

#### Phase 2/3

- Amphitheater lower seating concrete to be poured.
- Amphitheater parking lot cross walk and bollards to be installed.
- Picnic Pavilion concrete slabs to be poured.
- Final Grading of great lawn to be completed.
- Sensory Playground Material to arrive on site and begin install of equipment.

#### <u>Phase 4 – Community Center</u>

- Stucco and paint work to continue at exterior façade.
- Interior MEP rough in to continue install.
- Electrical rooms continue to be built out.
- Mechanical duct install at level 2 to begin installation.

#### Phase 4 – Aquatics Center

- Roofing at Support and Aquatics Buildings to be completed.
- Shell work at support building and grandstands to be completed.
- Myrtha system panels to be installed at competition pool.





## Doral Cultural Arts Center

#### **Project Information & Status**

Location: 8363 NW 53 St.

Doral FL 33166

**Budget:** \$10,890,911.97

Status: Completed


#### **Program Overview**

The Doral Cultural Arts Center site is located at 8363 NW 53 St. Doral FL 33166, adjacent to the City of Doral Government Center. This facility serves to celebrate the variety of cultures, arts, and experiences that make Doral so unique. Features include a large art gallery space, multi-purpose room, rooftop plaza, outdoor courtyard, catering room, and public restrooms.



Project Phase	Start Date	Finish Date
Procurement Process	Jul 2019	Sep 2019
Design	Sep 2019	May 2020
Construction	Mar 2021	Sep 2022
Closeout Project	Oct 2022	Jan 2024



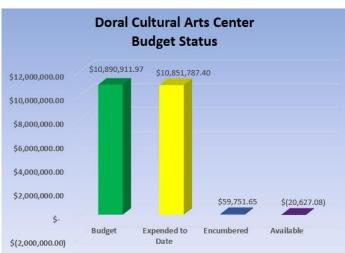



## Doral Cultural Arts Center



#### **Current Status**

Final project closeout being completed.





## Trails Network

#### **Project Information & Status**


**Location:** Construction of multipurpose trails throughout the City of Doral

**Budget:** \$2,336,495.92

**Status:** Design Development (Phase 2)

#### **Program Overview**

The project includes improvements and adding approximately 5 miles of multipurpose trails around the City of Doral. Existing segments enhancements will include trail lighting, pavement markings, and signage.

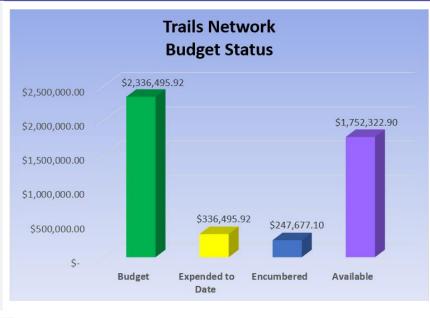



Project Phase	Start Date	Finish Date
Procurement Process	Apr 2020	May 2020
Design	May 2021	Oct 2020
Construction	Jul 2021	Mar 2022
Closeout	Feb 2022	Mar 2022



Project Phase	Start Date	Finish Date
Procurement Process	Jun 2023	July 2023
Design	Jul 2023	March 2024
Construction	TBD	TBD
Closeout Project	TBD	TBD




## Trails Network - Phase 2 (Lighting)

#### Phase 2 - Program Overview

It was determined to re-allocate approximately \$2,000,000 to the Trails Network project in order to complete lighting enhancements to existing trails as part of the Trails Network Project.

The current improvements include approximately 2.7 miles of bike trails. The trail lighting scope of work is being moved from the Pedestrian Bridge scope to the Trails Network scope, and additional improvements will be studied to reach the 5 miles of improvements.



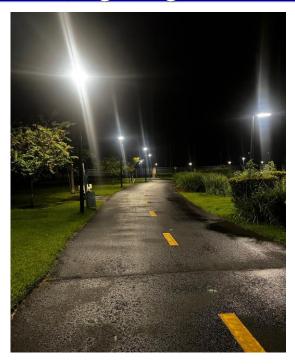

#### **Current Status**

Coordination with utility company (FPL) and authorities having jurisdiction continue. Conversations regarding Miami-Dade County approvals ongoing.



**AECON** 



## Prepared with the assistance of:



2 Alhambra Plaza Suite 900 Coral Gables, FL 33134 Tel: 305-447-3522

www.aecom.com



11606 City Hall Promenade Suite 200 Miramar, FL 33025 Tel: 954-237-7850 www.pds-eng.com
