



Doral Central Park

Recreation Center Feb 9th, 2023



Table of Contents

Program Overview	3
Project Complete	4
Program Progress Report	5
Timeline	6
Project Information & Status	
Doral Central Park	7,8,9
Doral Cultural Arts Center	10,11
Doral Meadow Park	12
Doral Pedestrian Bridge	13,14
Doral White Course Park	15
Morgan Levy Park	16
Trails and Tails Park	17
Trails Network	18,19
Upcoming Work	20




AECOM

Program Overview

On June 13, 2018, the City unanimously adopted Resolution No. 18-112 by the City Council authorizing the City to hold a bond referendum election for the purpose of determining whether most qualified electors voting in the election would approve the issuance of the City's general obligation bonds to finance the cost of the Parks and Recreation Projects. On November 6, 2018, the City of Doral residents voted to approve the referendum authorizing the City to issue general obligation bonds in an amount not to exceed \$150,000,000. These bonds are to be utilized for upgrading and building a system of world class parks, natural areas and recreational facilities. The Bond Referendum authorized the financing of the construction and improvement of parks and recreational facilities with safety features, including, but not limited to, green spaces, community centers, cultural amenities, aquatic facility, playgrounds, sports fields and approximately five miles of walking/cycling trails. The General Obligation Bond includes the following projects: the redevelopment of Doral Central Park, Doral Meadow Park renovation, the construction of the Doral Cultural Arts Center, the construction of Doral White Course Park, Morgan Levy Park improvements, the construction of the Pedestrian Bridge at 41st Street and 117th Avenue, lighting improvements for Trails and Tails Park, and bikeways/lighting improvements for various Trails Networks.



Projects Completed

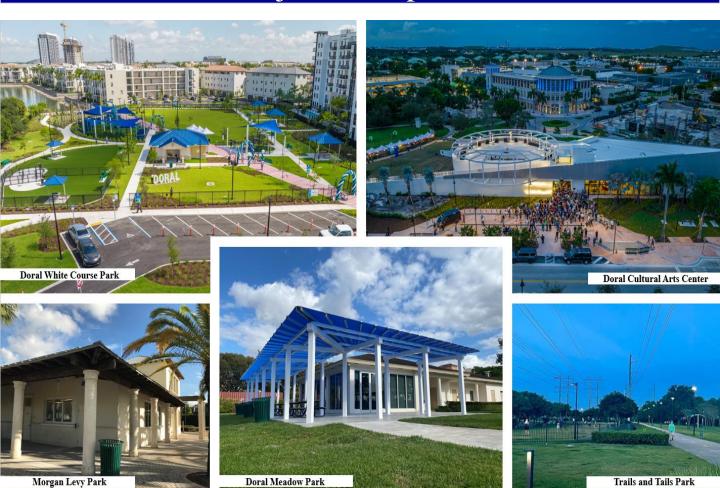




Program Progress Report


Project Name	Status	Start Date	Finish Date	Original Program Budget	Budget	Spent	Available
Doral Central Park	Under Construction	Feb 2020	Spring 2025	\$ 124,866,109.94	\$ 171,874,814.69	\$ 29,838,568.00	\$ 142,036,246.69
Doral Cultural Arts Center	Complete	Jul 2019	Spring 2023	\$ 9,905,187.96	\$ 10,759,127.21	\$ 10,685,104.60	\$ 74,022.61
Doral Meadow Park	Complete	Nov 2019	Aug 2021	\$ 1,561,659.00	\$ 1,875,689.39	\$ 1,875,689.39	s -
Doral Pedestrian Bridge	Pre-Construction	Dec 2020	TBD	\$ 6,189,257.92	\$ 8,732,866.27	\$ 494,750.81	\$ 8,238,115.46
Doral White Course Park	Complete	Sep 2019	Jul 2022	\$ 4,102,555.49	\$ 4,408,798.26	\$ 4,408,798.26	s -
Morgan Levy Park	Complete	Nov 2019	May 2021	\$ 704,637.92	\$ 825,199.13	\$ 825,199.13	s -
Trails and Tails Park	Complete	Dec 2019	Jul 2022	\$ 1,052,752.47	\$ 1,024,674.39	\$ 962,925.46	\$ 61,748.93
Trails Network	Design Development	Apr 2020	TBD	\$ 923,274.05	\$ 2,434,738.63	\$ 434,738.63	\$ 2,000,000.00

TOTAL \$ 149,305,434.75 | \$ 201,935,907.97 | \$ 49,525,774.28 | \$ 152,410,133.69

Budget

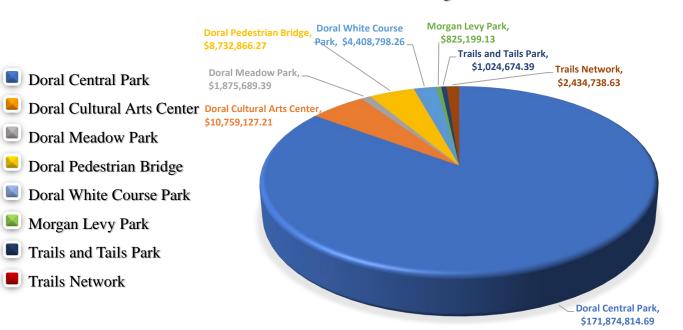



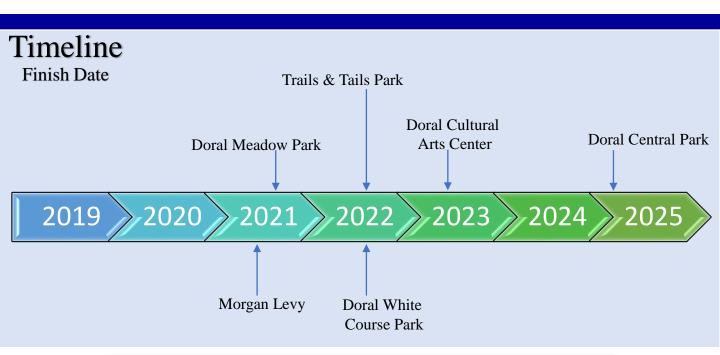

Project	Start Date	Finish Date
Doral Central Park	Feb 2020	Spring 2025
Doral Cultural Arts Center	Jul 2019	Spring 2023
Doral Meadow Park	Nov 2019	Aug 2021
Doral Pedestrian Bridge	Dec 2020	TBD
Doral White Course Park	Sep 2019	Jul 2022
Morgan Levy Park	Nov 2019	May 2021
Trails & Tails Park	Dec 2019	Jul 2022
Trails Network	Apr 2020	TBD







Doral Central Park

Project Information & Status

Location: 3000 NW 87 Ave. Doral FL 33172

2 0141 1 2 00 1 / 2

Budget: \$171,874,814.69


Status: Under Construction



Program Overview

Doral Central Park is located at 3000 NW 87th Avenue. The site is situated on 79 acres of which 21 are the lake. It will be largest park in the City, and one of the largest in the region. The park includes an 80,000 SF Recreational Center, Aquatics Facility, meandering paved paths connecting the tennis and basketball courts, picnic pavilions, playgrounds, beach volleyball courts, multi-purpose fields, skatepark and pump track, as well as an open-air Amphitheater for community and large-scale events. The lake has a canoe/kayak/paddleboard launch and boardwalk. Landscaping will add to the enjoyment of the park adding more shaded areas and pleasant views. The vehicular traffic pathways have roundabouts for ease of navigation for entrance/exit to the park with ample parking spaces.

Project Phase	Start Date	Finish Date
Procurement Process	Feb 2020	May 2020
Design	Apr 2020	Mar 2022
Phase 2 & 3 Construction	Aug 2022	Summer 2024
Phase 4 Construction	Mar 2023	Winter 2024
Closeout Project	Dec 2024	Spring 2025







Doral Central Park

Work completed in February 2023

Watermain tie-in at 87th Avenue finished with the completed restoration of the affected asphalt and sidewalk. Other sitework included finalizing the sewer laterals across the site and the start of drainage work by the Sensory Playground. Rebar and concrete were installed for the shade canopy foundation at the playground. At the beach volleyball and skatepark with pump track locations the installation of sports lighting was completed. Structural work at the Recreation Center continued with the installation of columns and beams in preparation to receive steel. Concurrently, the underground electrical and plumbing work were completed, and the slab on grade was placed at the gymnasium. Outbuilding C was prepped to receive slab on grade and tie-beams were finished; Outbuilding D to follow. The Amphitheater foundation/footings were completed, and the berm area received grading to provide an optimal view of the stage for future audiences. Work at the Aquatics Facility commenced with the start of deep soil mixing for the competition and training pool, and surge tank.



Aerial of Recreation Center Construction



Deep Soil Mixing at Aquatics Facility



Amphitheater Stage Foundation / **Footings**



Drainage at Sensory Playground



Columns and **Beams** at Recreation Center









Doral Central Park



Upcoming Work



Drainage work to continue at the north side of the site, along with installation of underground conduits along the North Road. Irrigation mainline installation to continue at the South-West Road, and grading to commence at the South Road. Construction of the Recreation Center to continue with structural work, concrete placements, steel delivery, and MEP work. Outbuildings C and D are slated to be completed in March. Deep soil mixing to continue at the Aquatics Facility for the competition and training pool, and surge tank. The foundations for the Aquatics Facility buildings are set to start.



Doral Cultural Arts Center

Project Information & Status


Location: 8363 NW 53 St. Doral FL 33166

Budget: \$10,759,127.21

Status: Completed


Program Overview

The Doral Cultural Arts Center site is located between 53rd Street and 53rd Terrace, adjacent to the City of Doral Government Center. This facility will serve to celebrate the variety of cultures, arts, and experiences that make Doral so unique. Features will include a large art gallery space, a multi-purpose room, outdoor courtyards, area for catering, and public restrooms.

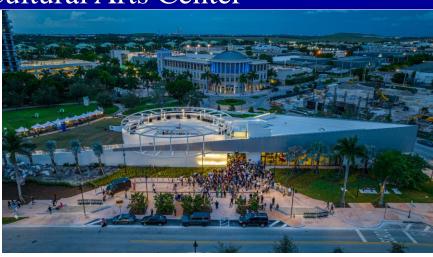


Project Phase	Start Date	Finish Date
Procurement Process	Jul 2019	Sep 2019
Design	Sep 2019	May 2020
Construction	Mar 2021	Sep 2022
Closeout Project	Oct 2022	Spring 2023



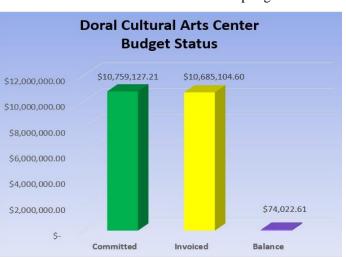



Upcoming Work

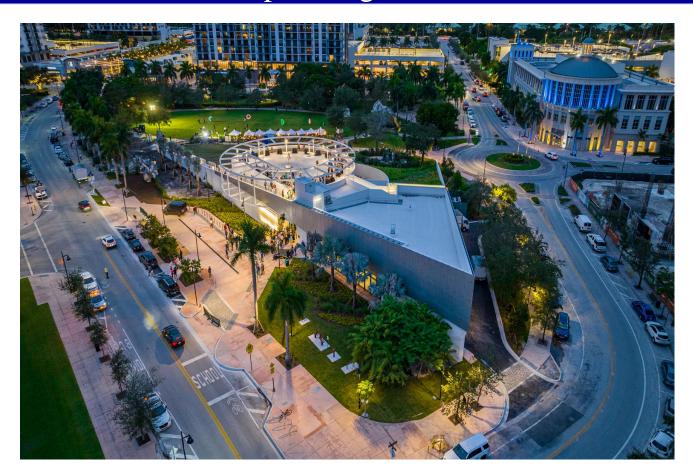

Current Status

Punchlist walkthrough's have been completed, pending minor corrective work from the contractor. Corrective work for sloped lawn pending change order approval, estimated to be completed by July 2023. Contractor working with Authorities having jurisdiction to close out final permits and achieve final certificate of occupancy.

Upcoming Work

Punchlist walkthroughs have concluded. Pending corrective work to sloped lawn, and final closing of contractor's permits for final Certificate of Occupancy.



Doral Meadow Park

Project Information & Status

Location: 11555 NW 58th St.

Doral, FL 33178

Budget: \$1,875,689.39

Status: Completed



Program Overview

The park is located at 11555 NW 58th Street, Doral, FL. The project includes enclosing the existing outdoor patio space to provide 800 square feet of indoor recreation area with a new HVAC system. In addition, the existing building renovation will include a high-tech conference room, a kitchenette, façade treatments, an indoor trophy case, modernized bathrooms and a multi-purpose outdoor plaza.

Project Phase	Start Date	Finish Date
Procurement Process	Nov 2019	Nov 2019
Design	Jan 2020	Jun 2020
Construction	Jul 2020	Jun 2021
Closeout Project	Jul 2021	Aug 2021







Doral Pedestrian Bridge

Project Information & Status

Location: The bridge will connect the north and south portions of the Turnpike Trail along NW 117th Avenue

New Budget: \$10,732,866.27

(\$10,732,866.27- \$2,000,000 being reallocated to Trails Network)

Status: Pre-Construction

Program Overview

The bridge will connect the north and south portions of the Turnpike Trail along NW 117th Avenue. The bridge will allow pedestrians and cyclists to safely cross over Doral Boulevard (41st Street). The bridge will provide ADA accessibility via ramps and elevators. A covered roof and open sided breeze way with lighting and security cameras will provide residents with an unobstructed view of the city.



Project Phase	Start Date	Finish Date
Procurement Process	Dec 2020	TBD
Design	TBD	TBD
Construction	TBD	TBD
Closeout Project	TBD	TBD







Doral Pedestrian Bridge



Current Status

During the February City Council meeting, it was determined to temporarily stall the Pedestrian Bridge project, due to escalation and budget issues and the FDOT concurrence. The City will be seeking additional funding for the project, to be announced in a future Council meeting. It was also determined in February meeting to re-allocate \$2,000,000 from this project's budget to the Trails Network project in order to improve/add trails for the Trails Network Project. The trail lighting scope of work will be moved from the Pedestrian Bridge scope to the Trails Network scope for this work.

Upcoming Work

Project pending additional funding to be announced in a future Council meeting. Additional, lighting scope of work has been moved from this project to the Trails Network.





Doral White Course Park

Project Information & Status

Location: 8429 NW 41 St. Doral, FL 33166

Budget: \$4,408,798.26

Status: Completed


DORAL

Program Overview

This Park is located at 8429 NW 41st Street in Doral, FL. This new park will include a shaded playground, a waterfront event plaza, outdoor fitness stations, a multi-purpose green space area, fenced-off dog area, restrooms, and shelters. The park will have limited landscape lighting with general overhead and walkway lighting and security cameras. A new boardwalk will connect this park to the Downtown Doral area.

Project Phase	Start Date	Finish Date
1 Toject I flase	Start Date	Tillish Date
Procurement Process	Sep 2019	Feb 2020
Design	Mar 2020	Sep 2020
Construction	Apr 2021	May 2022
Closeout Project	May 2022	Jul 2022



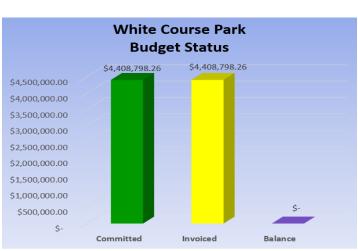



Morgan Levy Park

Project Information & Status

Location: 5300 NW 102nd Ave.

Doral, FL 33178

Budget: \$825,199.13

Status: Completed



Program Overview

Morgan Levy Park is located at 5300 NW 102nd Avenue, Doral, FL. This project involves the removal and replacement of existing flooring, new millwork, painting, and the addition of a grease interceptor. The addition of ADA accessible routes to the picnic areas and transitioning to higherficiency LED fixtures in the parking area as well as adding and enhancing security cameras.

The same of the sa	
555	

Project Phase	Start Date	Finish Date
Procurement Process	Nov 2019	May 2020
Design	Sep 2020	Apr 2020
Construction	Aug 2020	Feb 2021
Closeout Project	Mar 2021	May 2021







Trails and Tails Park

Project Information & Status

Location: 11645 NW 50th St.

Doral, FL 33178

Budget: \$1,024,674.39

Status: Completed



Program Overview

The park is located at 11645 NW 50th Street, Doral FL. The project includes the installation of additional light fixtures to increase security in the area, replace existing fixtures and or supports and add lighting to the dog and play areas.



Project Phase	Start Date	Finish Date
Procurement Process	Dec 2019	Nov 2020
Design	Dec 2020	Jul 2021
Construction	Aug 2021	Jun 2022
Closeout Project	Jun 2022	Jul 2022





Trails Network

Project Information & Status

Location: Construction of multipurpose trails and trails improvements throughout the City of Doral

New Budget: \$2,434,738.63

(Old budget was \$434,738.63 + \$2,000,000.00 reallocated from Pedestrian Bridge)

Status: Design Development




Program Overview

The project includes improvements and adding miles of multi-purpose trails around the City of Doral. Existing segments enhancements will include trail lighting, and pavement markings.

Project Phase	Start Date	Finish Date
Procurement Process	Apr 2020	TBD
Design	TBD	TBD
Construction	TBD	TBD
Closeout Project	TBD	TBD



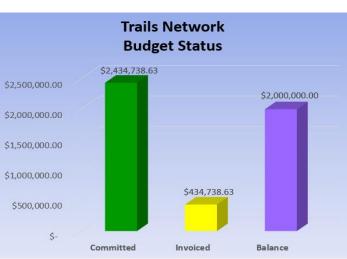



Trails Network



Current Status

It was determined to re-allocate approximately \$2,000,000 from the Pedestrian Bridge project budget to the Trails Network project in order to complete lighting enhancements to existing trails as part of the Trails Network Project. The current improvements include approximately 2.7 miles of bike trails. The trail lighting scope of work is being moved from the Pedestrian Bridge scope to the Trails Network scope, and additional improvements will be studied to reach the 5 miles of improvements.

Upcoming Work

During the February Council meeting, it was determined to re-allocate approximately \$2,000,000 from the Pedestrian Bridge project's budget to the Trails Network project in order to improve/add for the network. The trail lighting scope of work will be moved from the Pedestrian Bridge scope to the Trails Network scope for this work. Discussions are being held with design professionals, Parks Department, and PMT to determine path forward for this project.





Produced for the City of Doral by:

AECOM

2 Alhambra Plaza Suite 900 Coral Gables, FL 33134 Tel: 305-447-3522

www.aecom.com

PDS Inc.

11606 City Hall Promenade Suite 200 Miramar, FL 33025 Tel: 954-237-7850 www.pds-eng.com

PROGRAM MANAGEMENT TEAM









